

SIGN LEGEND:


(A)	WHITNEY AVE.	80-9919
	DETOUR	80-9707
	→	51-2626R
(B)	WHITNEY AVE.	80-9919
	DETOUR	80-9707
	←	51-2626L
(C)	WHITNEY AVE.	80-9919
	DETOUR	80-9707
	↑	51-2625
(D)	ROAD CLOSED WHITNEY AVENUE LOCAL TRAFFIC ONLY	80-9928
	BROADWAY TO DUNELLEN RD	80-9913
	DETOUR	80-9707
	→	51-2626R
(E)	ROAD CLOSED WHITNEY AVENUE LOCAL TRAFFIC ONLY	80-9928
	BROADWAY TO DUNELLEN RD	80-9913
	DETOUR	80-9707
	←	51-2625
(F)	ROAD CLOSED WHITNEY AVENUE LOCAL TRAFFIC ONLY	80-9928
	BROADWAY TO DUNELLEN RD	80-9913
	DETOUR	80-9707
	↑	51-2625
(G)	ROAD CLOSED TO THRU TRAFFIC	80-9081
	DETOUR	80-9702
	←	
(H)	DETOUR AHEAD	80-9933
(I)	ROAD CLOSED	80-9080
(J)	END DETOUR	80-9708

DETOUR NOTES:

1. ALL SIGN LOCATIONS INDICATED ON THIS PLAN ARE APPROXIMATE. EXACT LOCATIONS OF SIGNS SHALL BE DETERMINED IN FIELD AS DIRECTED BY THE ENGINEER.
2. DETOUR SIGNS SHALL BE COVERED WHEN THE DETOUR IS NOT IN OPERATION.
3. DETOUR SIGNS SHALL BE REMOVED WHEN THE DETOUR IS NO LONGER REQUIRED.
4. ALL CONSTRUCTION SIGNS ARE TO BE INSTALLED SUCH THAT THEY DO NOT BLOCK, OR ARE NOT BLOCKED BY, EXISTING SIGNS, AND DO NOT INTERFERE WITH SIGHT LINES.
5. EXISTING SIGNS WHICH CONFLICT WITH THE DETOUR SIGNS SHALL BE COVERED WHILE THE DETOUR IS IN EFFECT, AS DIRECTED BY THE ENGINEER.
6. BARRICADE WARNING LIGHTS - HIGH INTENSITY SHALL BE MOUNTED ON ALL DIAMOND SHAPED POST-MOUNTED CONSTRUCTION SIGNS AND SIGN (I).
7. CONTRACTOR TO NOTIFY THE TOWN OF TRUMBULL EMERGENCY SERVICES TWO WEEKS PRIOR TO THE CLOSURE.
8. THE COST OF DETOUR SIGNS SHALL BE PAID FOR UNDER THE ITEM "CONSTRUCTION SIGNS".
9. RELOCATION OF TEMPORARY PRECAST CONCRETE BARRIER CURB FOR ACCESS TO WORK AREA SHALL NOT BE MEASURED FOR PAYMENT.
10. MAINTAIN ACCESS TO ALL DRIVEWAYS DURING CONSTRUCTION.

SYMBOL LEGEND:

- SINGLE POST MOUNTED SIGN
- DOUBLE POST MOUNTED SIGN
- DIRECTION OF TRAFFIC
- CONSTRUCTION BARRICADE TYPE III
- ▬ TEMPORARY PRECAST CONCRETE BARRIER CURB

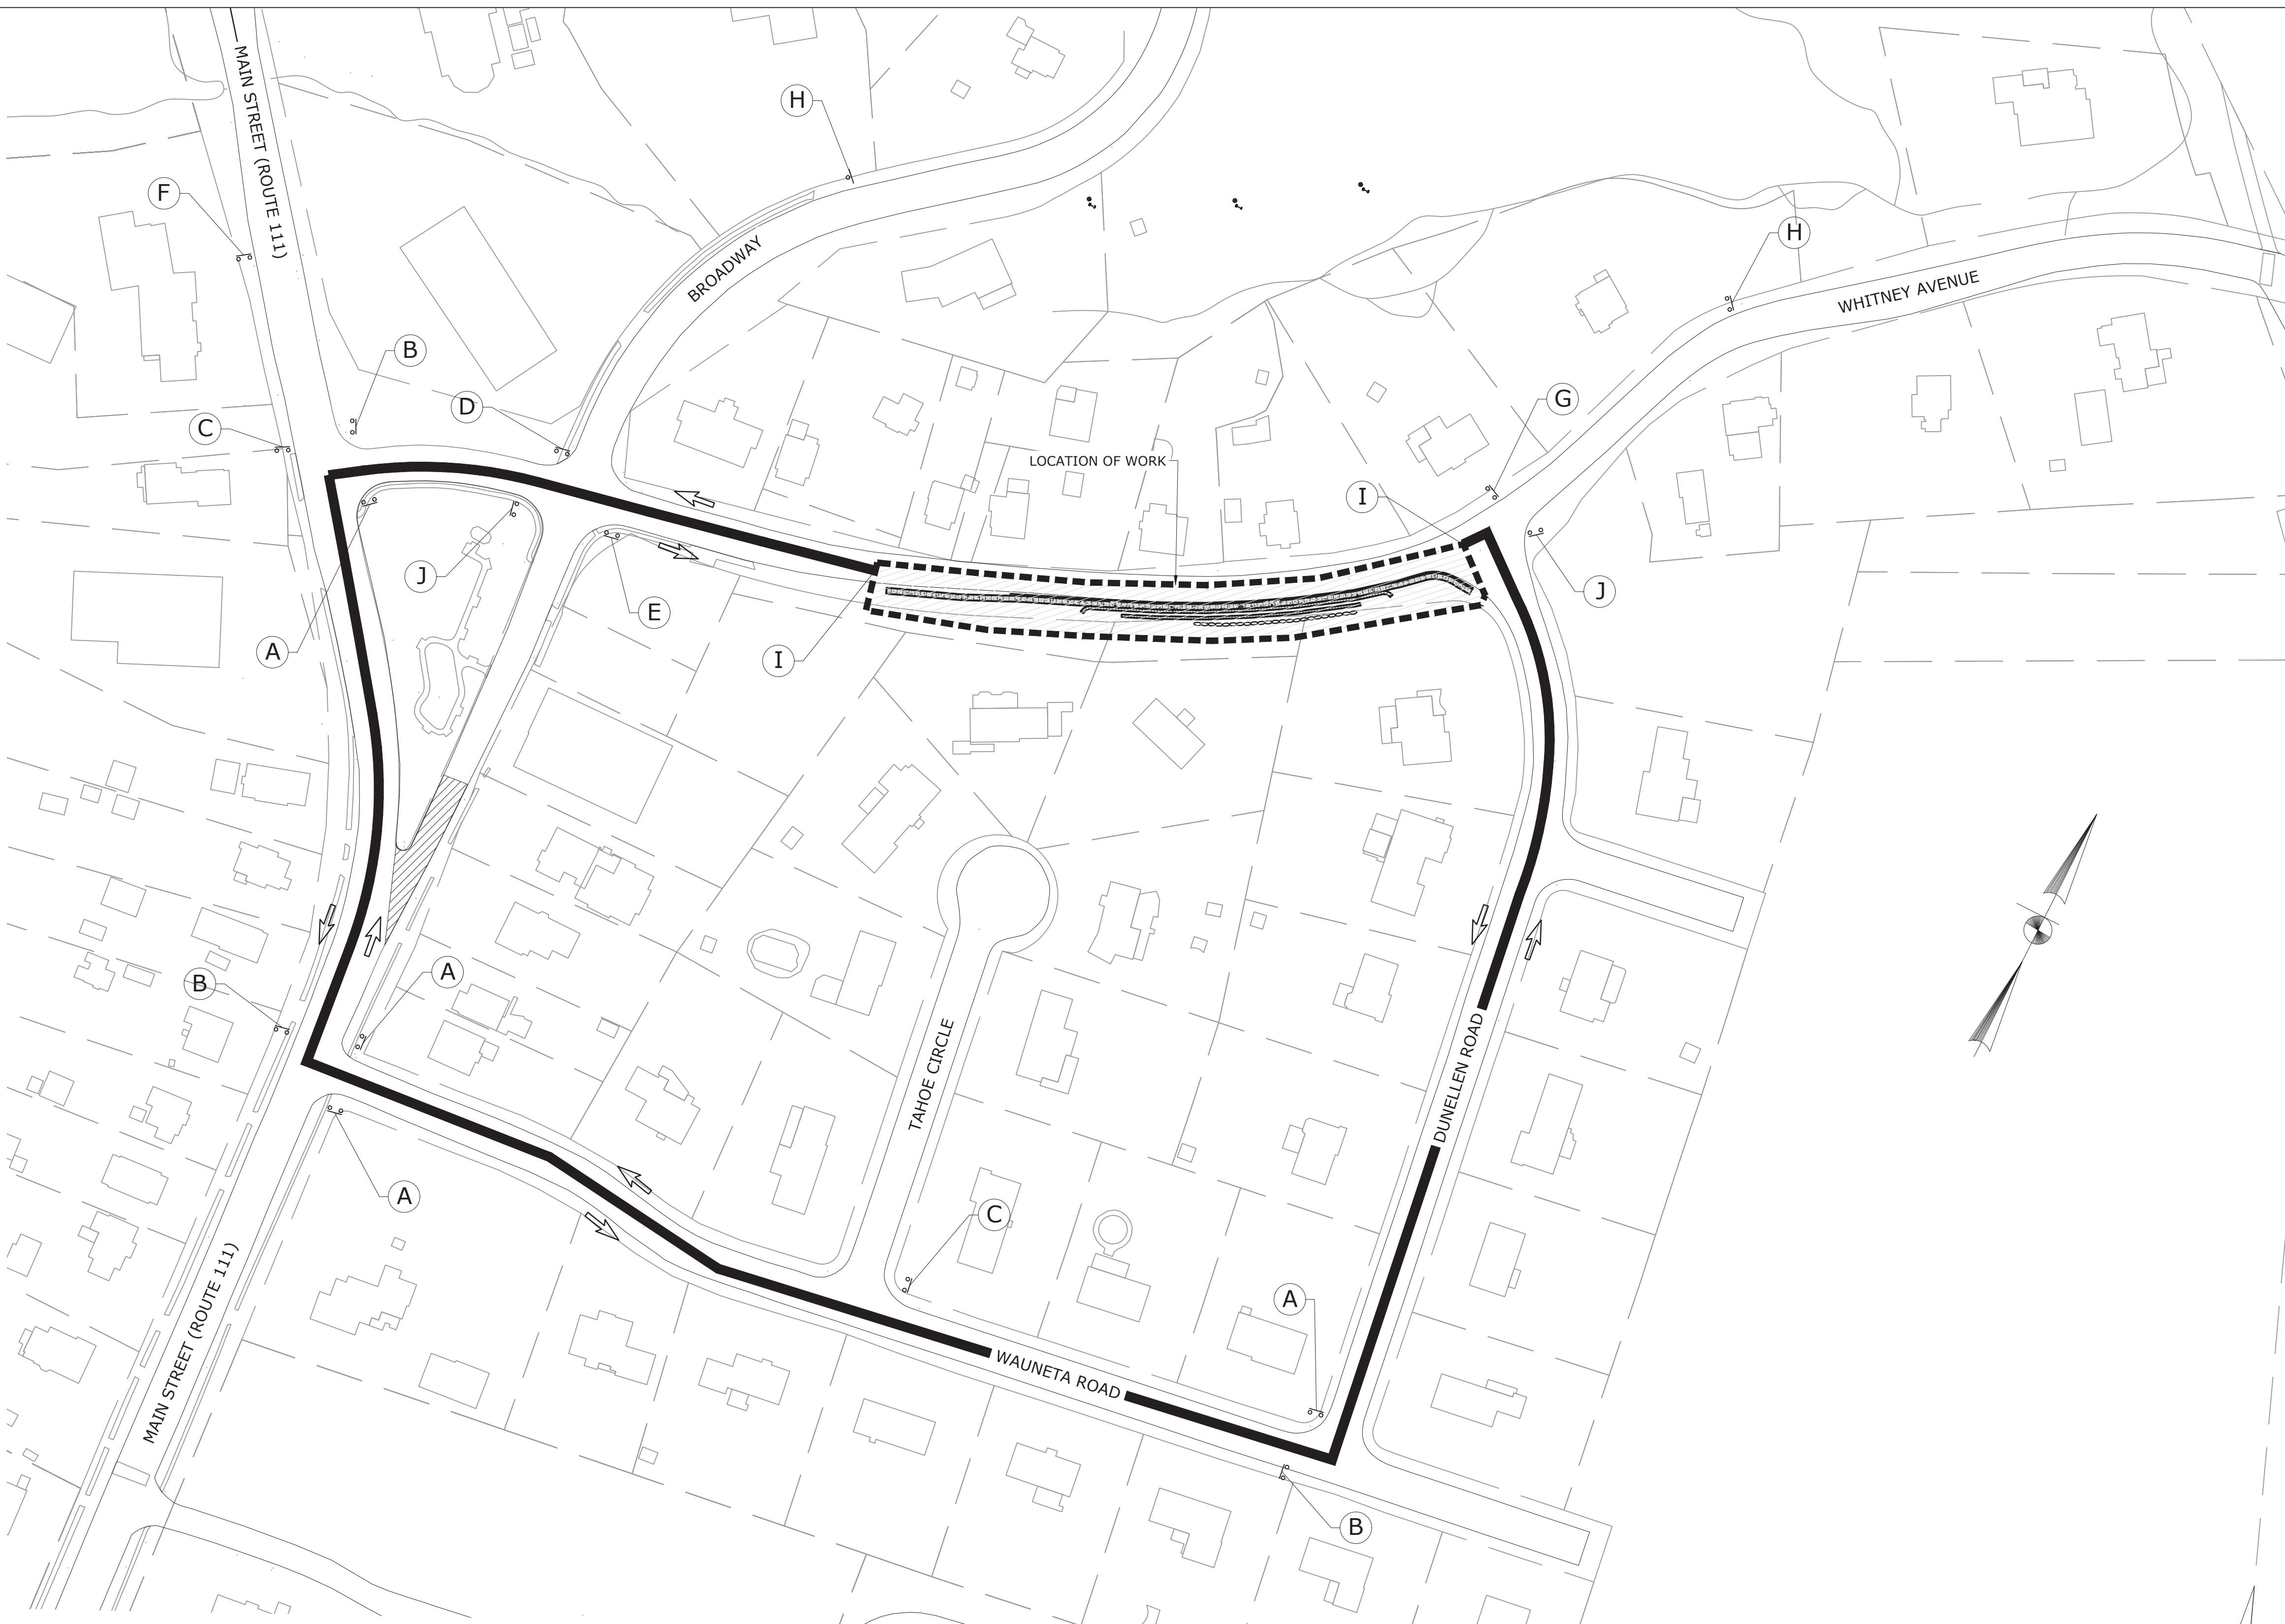

MAINTENANCE AND PROTECTION OF TRAFFIC PLAN

SCALE: 1"=20'


-	-	-	-	THE INFORMATION, INCLUDING ESTIMATED QUANTITIES OF WORK, SHOWN ON THESE SHEETS IS BASED ON LIMITED INVESTIGATIONS BY THE TOWN AND IS IN NO WAY WARRANTED TO INDICATE THE CONDITIONS OF ACTUAL QUANTITIES OF WORK WHICH WILL BE REQUIRED.
-	-	-	-	
-	-	-	-	
-	-	-	-	
-	-	-	-	Plotted Date: 7/8/2020
REV. DATE	REVISION DESCRIPTION	SHEET NO.	Stantec Project No.: 192311043	

THE INFORMATION, INCLUDING ESTIMATED QUANTITIES OF WORK, SHOWN ON THESE SHEETS IS BASED ON LIMITED INVESTIGATIONS BY THE TOWN AND IS IN NO WAY WARRANTED TO INDICATE THE CONDITIONS OF ACTUAL QUANTITIES OF WORK WHICH WILL BE REQUIRED.

Plotted Date: 7/8/2020

Stantec Project No.: 192311043

DESIGNER/DRAFTER: KPG  
CHECKED BY: PJK  
SCALE IN FEET  
0 20 40  
SCALE 1"=20'



**TOWN OF TRUMBULL  
CONNECTICUT**



Stantec Consulting Services Inc.  
55 Church Street, Suite 601  
New Haven CT 06510  
Tel. 203.495.1645  
Fax. 203.495.1652  
www.stantec.com

PROJECT TITLE:  
**WHITNEY AVENUE  
SIDEWALK IMPROVEMENTS**

TOWN:  
**TRUMBULL**  
DRAWING TITLE:  
**MPT PLAN**

PROJECT NO.  
**TR-01**  
DRAWING NO.  
SHEET NO.  
**04.01**
